

**MANAGING CONSTRUCTION DISPUTES**

CALEB DUMISA MOTSA

A master's report submitted as a partial fulfillment of  
the requirement for the award of degree of  
Master of Science (Construction Management)

Faculty of Civil Engineering  
Universiti Teknologi Malaysia

November, 2006

## **ACKNOWLEDGEMENT**

I would like to express my sincere gratitude and grateful appreciations to my supervisor, Dr Rosli Mahamad Zin for his invaluable guidance, advice, encouragement and help throughout the project. Without his advice and constructive ideas this report wouldn't be successfully accomplished.

A special acknowledgement must be given to my sponsor the Common Wealth Scholarship under the Government of Malaysia, for their financial support throughout this project.

## **ABSTRACT**

Construction projects are increasingly complex, resulting in complex contract documents. Complex construction can likewise result in complex disputes. Disputes is inevitable in construction projects which predominantly arise from complexity and magnitude of works, multiple prime contracting parties, poorly prepared and/ or executed contract documents, inadequate planning, financial issues and communication problems. Any of these factors can overturn a project and lead to complicated litigation, arbitration, mediation, time overrun, increased costs and a relationship break down among members of different parties involved. The objectives of this study are to identify the root causes of construction disputes as well as their impact on client's organization. The methodology of study adopted was through questionnaire survey where the target respondents were clients, consultants and contractors. Based on the analyzed data, there are nine root causes of construction disputes caused by clients, five root causes caused by consultants and four root causes caused by contractors have been identified in the local construction industry. The impact of construction disputes in client's organization as found in the study are time consuming, cost effective, loss of reputation and sour relationship between stakeholders and also loss of profit and business validity. ADRs were observed as the best method of resolving disputes because they were identified as none time consuming and cost effective. From the findings it can be concluded that construction disputes are a cause of concern in every project and the solution to this problem is to avoid and cautiously manage them for smooth running of construction process, prevention is believed is better than cure.

## ABSTRAK

Projek pembinaan masa kini didapati semakin rumit dan kompleks, di mana ini sedikit sebanyak turut menyebabkan dokumen kontrak juga menjadi semakin rumit dan kompleks. Projek pembinaan yang kompleks ini juga menghasilkan pertelingkahan yang kompleks. Pertelingkahan adalah sesuatu yang tidak dapat dielakkan kerana ia pada asasnya timbul disebabkan oleh keadaan kerja yang kompleks serta magnitud kerja-kerja tersebut, selain penglibatan ramai pihak di dalam sesebuah kontrak, kualiti yang kurang memuaskan dalam penyediaan dan penggunaan dokumen kontrak, perancangan yang tidak mencukupi, isu-isu kewangan serta masalah-masalah komunikasi. Salah satu daripada faktor-faktor tersebut sudah mencukupi untuk menggagalkan sesuatu projek serta menyebabkannya menghadapi proses-proses rumit yang melibatkan perundangan, timbangtara, dan mediasi, di samping menyebabkan kelewatan penyediaan projek, peningkatan kos keseluruhan projek serta menjejaskan hubungan di kalangan pihak-pihak yang terlibat dalam projek tersebut. Objektif bagi kajian ini adalah untuk mengenalpasti penyebab utama pertelingkahan di dalam projek pembinaan selain mengenalpasti impaknya terhadap organisasi klien. Metodologi yang digunakan di dalam kajian ini adalah melalui borang soal selidik di mana responden-respondennya terdiri daripada pihak klien, perunding projek serta kontraktor. Berdasarkan kepada data-data yang telah dianalisis, di dalam industri pembinaan tempatan, dikenalpasti terdapat sembilan penyebab utama pertelingkahan di dalam projek pembinaan berpunca daripada pihak klien, manakala lima lagi penyebab utamanya adalah berpunca daripada pihak perunding projek serta empat lagi penyebab utama pertelingkahan di dalam projek pembinaan adalah berpunca daripada pihak kontraktor. Impak pertelingkahan di dalam projek pembinaan bagi organisasi klien yang dikenalpasti melalui kajian ini adalah ianya memakan masa, menelan belanja, hilangnya reputasi dan mengakibatkan hubungan yang renggang di kalangan pihak-pihak yang terlibat, selain mengakibatkan kerugian serta melemahkan perniagaan yang dijalankan. ADR didapati merupakan kaedah yang terbaik untuk menyelesaikan pertelingkahan kerana ia didapati tidak memerlukan masa yang panjang serta kosnya yang efektif. Daripada hasil kajian, boleh disimpulkan bahawa

pertelingkahan dalam projek pembinaan adalah sesuatu yang dititikberatkan dalam perkara kajian dan penyelesaian bagi masalah ini adalah dengan mengelakkan pertelingkahan bermula serta langkah-langkah awal untuk menguruskannya agar projek pembinaan dapat dilaksanakan secara lancar, kerana adalah dipercayai bahawa mengelak adalah lebih baik daripada mengatasi.

## TABLE OF CONTENTS

CHAPTER	TITLE	PAGE
<b>1</b>	<b>INTRODUCTION</b>	1
	1.1 Introduction	1
	1.2 Problem Statement	2
	1.3 Aim and Objectives	3
	1.4 Scope of Research	3
	1.5 Project Methodology	3
	1.6 Significance of Findings	5
	1.7 Summary	5
<b>2</b>	<b>LITERATURE REVIEW</b>	6
	2.1 Introduction	6
	2.2 Definition of Dispute	7
	2.3 Causes of Disputes in the Industry	8
	2.3.1 The Contract Conditions	10
	2.3.2 The Design Deficiency	18
	2.3.3 The Construction Process	28
	2.3.4 The Consumer Reaction	29
	2.3.5 Time	33
	2.4 Causes of Disputes by Stakeholders	34
	2.4.1 Causes of Disputes by Client	35
	2.4.2 Causes of Disputes by Consultants	36
	2.4.3 Causes of Disputes by Contractors	37
	2.5 The Impact of Construction disputes on client organization	39

	2.6 Methods of Recovery of Disputes	40
	2.6.1 Litigation	41
	2.6.2 Arbitration	41
	2.6.3 Mediation	42
	2.6.4 Negotiation	42
	2.7 Summary	43
<b>3</b>	<b>RESEARCH METHODOLOGY</b>	44
<b>4</b>	<b>DATA ANALYSIS AND RESULTS</b>	49
	4.1 Introduction	49
	4.2 Results and findings	60
	4.3 Analysis and Discussions	66
	4.3.1 Causes of disputes by clients	68
	4.3.2 Causes of disputes by consultants	72
	4.3.3 Causes of disputes by contractors	75
	4.3.4 The impact on client's organization	79
	4.3.5 The most preferred method of resolving disputes	81
	4.5 Summary of findings	82
	4.5.1 Identify the causes of major contributors of construction disputes	83
	4.5.2 Identify the impact of construction disputes in client's organization	85
	4.5.3 The most preferred method of solving disputes	85
<b>5</b>	<b>CONCLUSIONS AND RECOMMENATIONS</b>	86
	5.1 Introduction	86
	5.2 Conclusions	86
	5.3 Recommendations	88

<b>REFERENCES</b>	89
<b>APPENDICES</b>	92



**LIST OF FIGURES**

<b>Figure No.</b>	<b>Title</b>	<b>Page</b>
2.1	Causes of disputes in contract condition	17
2.2	Causes of disputes through design deficiency	27
2.3	Causes of disputes by client	35
2.4	Causes of disputes by designers	36
2.5	Causes of disputes by contractors	37
	Causes of construction disputes	38
2.7	Project dispute resolution satisfaction	40
4.1	Major causes of disputes caused by clients	71
4.2	Major causes of disputes caused by consultants	75
4.3	Major causes of disputes caused by contractors	77
4.4	Impact of disputes in client's organization	80
4.5	Major Root causes of construction disputes	83

## LIST OF TABLES

<b>Table No.</b>	<b>Title</b>	<b>Page</b>
	Causes of construction disputes caused by client	
4.1	i) Clients Point of View	54
4.2	ii) Consultants Point of View	55
4.3	iii) Contractors Point of View	56
4.4	iv) Overall respondents	57
	Causes of construction disputes caused by Designers	
4.5	i) Clients Point of View	58
4.6	ii) Consultants Point of View	59
4.7	iii) Contractors Point of View	60
4.8	iv) Overall Respondents	61
	Causes of construction disputes caused by contractors	
4.9	i) Clients Point of View	62
4.10	ii) Consultants Point of View	63
4.11	iii) Contractors Point of View	64
4.12	iv) Overall Respondents	65
	The Impact of Disputes in Clients Organization	
4.13	i) Clients Point of View	66
4.14	ii) Consultants Point of View	67
4.15	iii) Contractors Point of View	68
4.16	iv) Overall Respondents	69
4.17	The Most Preferred Method of Resolving Disputes	70

## **Chapter 1**

### **INTRODUCTION**

#### **1.1 Introduction to the Problem**

Construction relationships in the construction industry all over the world have become more increasingly strained as years goes on and on. Working relationships, communications, and contractual commitments are often not carried in good faith. This has led to most developed countries to search for better alternatives on how to manage disputes in the construction industry. Though it has been seen that disputes in the industry is like an un-incurable disease, means are done to fight the problem.

In the United Kingdom, for example the standard form of contract that is internationally used to new engineering contracts has been subject to change; whereas, in the United States of America the Disputes Review Boards ( DRB's) which comprises of three board members to manage disputes in construction sites was introduced. All this exercises undertaken have proved to be successful.

Developing countries are still facing this problem and the research on this topic will be on what to do either to improve or avoid and manage disputes in our local construction industry. Alternative dispute resolution is therefore essential for the industry in order to improve its performance.

## 1.2 Problem Statement

The construction industry has become very complicated such that political and economic trends are increasing the economic pressure resulting in disputes. Complex construction has brought about complex disputes in the industry. There are so many different types of sources that may lead to disputes and this eventually becomes a burden to the industry in terms of production

Great concern has been expressed in the recent years regarding the dramatic conflicts and disputes in the construction industry in the whole world and this has resulted in extensive high costs and time consuming. This is a result of the systems of resolving disputes in the industry. An alternative resolution has been seen as a necessity in the industry.

The alternative resolution of disputes should therefore address the causes of disputes within a limited space of time so that the production capacity is not affected in anyways. We have seen stakeholders blaming each other because of problems they come across during the construction process, because of poorly done designs, claims, poor administration and delays and these have been overlooked. There are questions rose on what is it that is actually causing disputes in the industry? And why disputes have become a nature of event in the industry?

Disputes and conflicts have gained frequent rise during construction of projects and this needs an involvement of a neutral body to resolve disputes as early as possible.

### **1.3 Aim and Objectives**

The aim of this study is to identify the best dispute resolution amongst the ones in current use, and objectives of the study will be summarized as follows:

- i To identify the root causes of construction disputes
- ii To identify the impact of disputes in the industry
- iii To identify dispute resolution methods.

### **1.4 Scope of Research**

This research has been carried out with a careful study on data collected mainly on case studies and questionnaire survey exercise. The research was focused on the private and government projects which are faced with the problem of construction disputes.

### **1.5 Project Methodology**

The methodology of the project consists of two phases as shown below (Refer to Figure 1.1):

#### **i) Phase one**

Gather information from journals, internet and book .Literature review on causes of construction disputes, the impact in Client's Organization and methods of dispute recovery.

**ii) Phase two**

The second phase of the study was conducting a survey and discussions with relevant stakeholders, data collection from relevant stakeholders, data analysis and discussions, conclusions and recommendations. The flow chart below illustrates the steps of the study (research methodology):

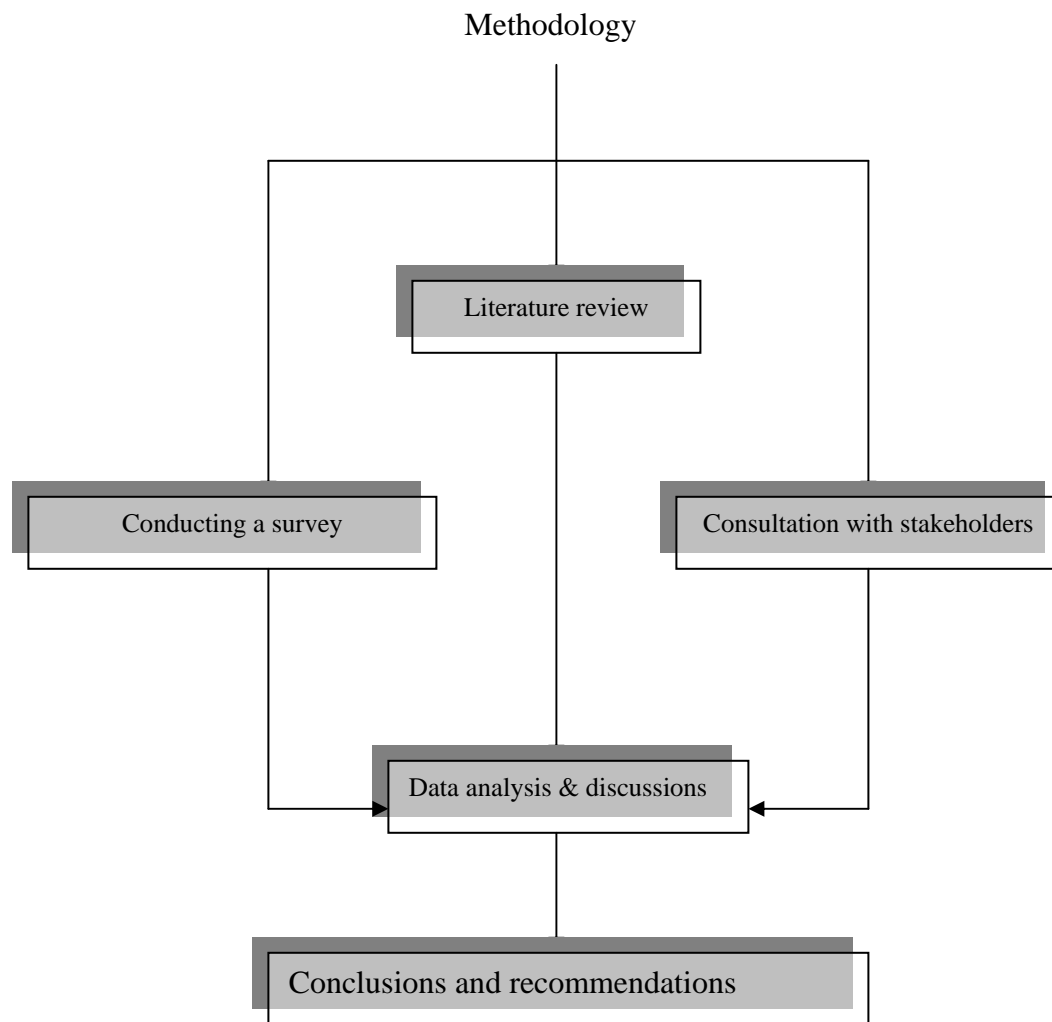


Figure.1.1: Research Methodology

## **1.6 Significance of Findings**

This study has identified the root causes of construction dispute caused by the client, designers and contractors. It also covers the impact of construction disputes in a client's organization and methods of disputes recovery. These factors had been seen as the major factors in affecting production in the industry, thus it is a necessity to manage them or rather to avoid them for the better part of the performance of the industry.

## **1.7 Summary**

This chapter covered the introduction to the problem of disputes in the construction industry that has prompted to this study. Moreover it states the aim and objectives, scope, methodology used and the significance of the findings. This project is based on managing construction disputes that has been seen to be affecting the industry's performance. The results to be obtained from the study will help in improving the production of the industry by means of implementing the decisions obtained from the results of the study.

## REFERENCES

- Association of Soil and Foundation Engineers (ASFE). (1995a). Annual strategic plan 1995-1996, Silver Spring, Md.
- Association of Soil and Foundation Engineers (ASFE). (1995b). Loss prevention through project management. Professional Firms Practicing in the Geosciences, ASFE, Silver Spring, Md.
- Bachner, J. (1995). Alternative dispute resolution: Successful new approaches to ancient problems, a message to client from ASFE. Association of Soil and Foundation Engineers, Silver Spring, Md.
- Bachner, J. (1988). ADR, alternative dispute resolution for the construction industry, 18 Association of Soil and Foundation Engineers, Silver Spring, Md 18.
- Battelle, A.E. (1995). The growing impact of AD on the construction industry: 'Real Time' dispute processing on the Boston Central Artery/ Tunnel Project. *Constr. Law*, Nov. 13.
- Boston's CA/T project warrants a better review. (1997). *Eng. News Rec.* 239(6), 94.
- Carmicheal, D.G. (2002). Disputes and international projects. Liisse: A.A. Balkema Publishers
- Carr, F., Lockwood, K. M., McDade, J., and Ruttinger, G. D. (1995). The untapped potential of ADR in the construction industry. *Fed. Law*, 42(32), note 3, 36.
- Cheeks, J. R. (1996). Settlements of shallow foundations on uncontrolled mine spoil fill, *J. Perform. Constr. Facil.*, 10(4), 143-151.
- Cheung, S.O., Tam, C.M. and Harris, F.C. Project Dispute Resolution Satisfaction Classification through Neural Network. 70 *Journal of Management in Engineering*, ASCE, January/ February 2000.
- Essex, J. R. (1996). Means of avoiding and resolving disputes during construction. Elsevier science Ltd: Tunneling and underground space technology. Vol. 11, No.i. 27-31
- Fenn, P. Lowe, D. and Speek C. Conflict and dispute in construction. Contract Management Economics. *Journal of Management in Engineering*, ASCE, Vol. 18No. 1:20, November 1997.



Groton, J. P. (1996). A new, comprehensive approach to dispute avoidance and resolution. Charting the course to the year 2000-Together, A landmark international multidisciplinary conference on dispute avoidance and resolution in the construction industry, 4. Univ. Of Kentucky, Lexington, Ky.

Goyal, B.B. construction claims and disputes. Causes and cost/ time overruns. *Journal of Construction Engineering and Management*, ASCE, 195-196, February/ March 1996.

Groton, J. (1991). Preventing and Resolving Construction Disputes, CPR Legal Program Construction Disputes Committee, center for Public Resources, New York, N.Y.

Hall, J.M. (2002). Ineffective communication: Common causes of construction disputes. Alliance's Advisory Council Legal Notes. Vol. 13, No.2

Hellard, B.R. (1997). *Preventing and solving construction contract disputes*. Litton educational publishing company.

Hohns, M.H. (1979). *Preventing and solving construction disputes*. New York: van Nostrand Reinhold Company.

Hall, J.M. (2002). Ineffective communication: Common causes of construction disputes. Alliance's Advisory Council Legal Notes. Vol. 13, No.2

Jessup, W. E., Jr., and Jessup, W.E. (1963). Law and specifications for engineers and scientists, 28-29.

McManamy, R. (1994). "Industry pounds away at disputes." Eng. News, 24,3.

Mix, D.M. (1997). ADR in the construction industry: Continuing the development of a more efficient dispute resolution mechanism.' Ohio St J. on Disp. Resol., 12, 463-464.

Ruskin, A. M., and Estes, W. E. (1982). What every engineer should know about project management, Association of Soil and Foundation Engineers, Silver Spring, Md., 14.

Smith, R. F., MacPherson, R.j., and Thomson, D. B. (1996). Dysfunctional ADR: Tips to avoid the pain." Constr. Lawyer, 16(26), 29-30.

Stipanowich, R.j. (1996). Beyond arbitration: Innovation and evolution in the United States construction industry. Wake forestl. Rev., 31, 65.

Stipanowich, T.J. (1998a). Reconstructing construction law: Reality and reform in a transactional system. Wis. L. Rev., 463-465.

Stipanowich, T.J. (1998b). The multi-door contract and other possibilities Ohio St. J. On Disp. Resol., 13, 303-32
